

PROGRESS UPDATE

• **COMPLETED WORK:**

- Precast Sequence 6
- Steel Elevator Tower
- Elevator Topping Slabs
- Installation of FDC's

• **ON-GOING WORK:**

- Precast Sequence 7,8,9
- Precast Welding & Grouting
- Running Electrical Conduit
- Installation of Lighting Boxes
- Setting of Plumbing Drains
- Wire Mesh
- Mock-Up
- SOG Prep
- Topping Slabs

• **UP-COMING WORK**


- Precast Sequence 10
- Hangers for Sprinklers
- Precast Caulking

Meetings

- Weekly Coordination Meeting
– Bi-Friday's @9:00 am
- Commissioning Meeting
– Monthly on the first Wednesday @11:00 am

DESCRIPTION	RESPONSIBILITY	DUE DATE	STATUS
<u>Safety – Blue Vest Safety Walks</u>			
<u>Coordination Items</u>			
Mock-Up	HRD / BC		Construction of Mock-Up has started. Date for Arch Finishes Review is 3/14.
GA Power Transformer	BC		Team met with GA Power on 1/22 to coordinate delivery and installation of the transformer.
Sign Coordination	NSH / BC		Team is in coordination the column color/sign diagram with the painter and the power requirements for the signs with the electrician.
Commissioning Meeting	NSH / BC / HRD		Team met 2/5 and discussed procedures and expectations moving forward for the commissioning of the MEP Systems.
Sprinklers	BC / HRD		Team met with the Sprinkler Contractor to on site Friday and has been coordinating daily any issues that have come up. – Target date to receive revised Shop Drawings 3/5.

PROGRESS PHOTOS

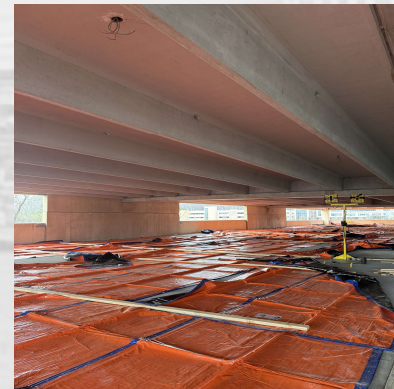

RFI's & Submittals

Total Open Submittals: 19

- #117/189 - Curtain Wall - Shop Drawings & Calculations
- #181 - 05 12 00 - 11 - Canopy Steel - Shop Drawings

Total Open RFI's : 8

- RFI #130 - Roof Parapet Steel
- RFI #128 - Roof Hatch Fire Rating
